

Appendix D

MaineDOT Tiger Grant Projects 2017

Project schedule

| ID | Task Mod | Task Name | Duration | Start | Finish | Predecessors | Project schedule | | | | | | | |
|----|----------|----------------------------------|----------|--------------|--------------|--------------------|------------------|-----|-----|-----|----------|-----|-----|-----|
| | | | | | | | Sep | Oct | Nov | Dec | 1st Half | Jan | Feb | Mar |
| 1 | | Project Kickoff | 0 days | Mon 9/18/17 | Mon 9/18/17 | | | | | | | | | |
| 2 | | Gather existing project data | 3 wks | Mon 9/18/17 | Fri 10/6/17 | 1 | | | | | | | | |
| 3 | | Initial Team meeting | 0 days | Fri 10/6/17 | Fri 10/6/17 | 1FS+3 wks,2 | | | | | | | | |
| 4 | | Preliminary Public Meeting | 0 days | Fri 11/17/17 | Fri 11/17/17 | 3FS+6 wks | | | | | | | | |
| 5 | | Survey completed | 6 wks | Mon 9/25/17 | Fri 11/3/17 | 3FS-10 days | | | | | | | | |
| 6 | | Hydraulic Analysis completed | 6 wks | Mon 11/6/17 | Fri 12/15/17 | 5 | | | | | | | | |
| 7 | | Preliminary Geotechnical work | 11 wks | Mon 11/6/17 | Fri 1/19/18 | 5 | | | | | | | | |
| 8 | | Preliminary Design Completed | 39 wks | Wed 11/29/17 | Tue 8/28/18 | 1,6FS-13 days | | | | | | | | |
| 9 | | Draft PDR completed | 0 days | Tue 8/28/18 | Tue 8/28/18 | 8 | | | | | | | | |
| 10 | | PDR reviewed, amended & | 12 wks | Wed 8/29/18 | Tue 11/20/18 | 9 | | | | | | | | |
| 11 | | Preliminary Design Report | 0 days | Tue 11/20/18 | Tue 11/20/18 | 10 | | | | | | | | |
| 12 | | Formal Public meeting | 0 days | Tue 1/1/19 | Tue 1/1/19 | 11FS+6 wks | | | | | | | | |
| 13 | | Utility Coordination | 12 wks | Wed 1/2/19 | Tue 3/26/19 | 12 | | | | | | | | |
| 14 | | Approach plans completed | 14 wks | Wed 1/2/19 | Tue 4/9/19 | 12 | | | | | | | | |
| 15 | | Plan Impacts Complete | 0 days | Tue 4/9/19 | Tue 4/9/19 | 14 | | | | | | | | |
| 16 | | Final Environmental Coordination | 41 wks | Wed 4/10/19 | Tue 1/21/20 | 15 | | | | | | | | |
| 17 | | Structural Design Completed | 74 wks | Wed 2/27/19 | Tue 7/28/20 | 15FS-30 days | | | | | | | | |
| 18 | | Utilities Certified | 8 wks | Wed 4/10/19 | Tue 6/4/19 | 15 | | | | | | | | |
| 19 | | ROW coordination | 62 wks | Wed 4/10/19 | Tue 6/16/20 | 15 | | | | | | | | |
| 20 | | NEPA complete | 0 days | Tue 1/21/20 | Tue 1/21/20 | 16 | | | | | | | | |
| 21 | | Environmental Approvals Complete | 22 wks | Wed 1/22/20 | Tue 6/23/20 | 20 | | | | | | | | |
| 22 | | PS&E package complete | 0 days | Tue 7/28/20 | Tue 7/28/20 | 19FS+2 days,21,17, | | | | | | | | |

Project: Tiger Project Schedule
Date: Fri 10/13/17

| | | | | | |
|--------------------|--|-----------------------|--|--------------------|--|
| Task | | Inactive Summary | | External Tasks | |
| Split | | Manual Task | | External Milestone | |
| Milestone | | Duration-only | | Deadline | |
| Summary | | Manual Summary Rollup | | Progress | |
| Project Summary | | Manual Summary | | Manual Progress | |
| Inactive Task | | Start-only | | | |
| Inactive Milestone | | Finish-only | | | |


MaineDOT Tiger Grant Projects 2017

Project schedule

| ID | Task Mod | Task Name | Duration | Start | Finish | Predecessors | Project schedule | | | | | | |
|----|----------|--------------------|----------|--------------|--------------|--------------|------------------|-----|-----|-----|-----------------|-----|-----|
| | | | | | | | Sep | Oct | Nov | Dec | 1st Half Jan | Feb | Mar |
| 23 | | Advertise | 0 days | Wed 8/26/20 | Wed 8/26/20 | 22FS+4.1 wks | | | | | | | |
| 24 | | Bid Opening | 0 days | Wed 9/16/20 | Wed 9/16/20 | 23FS+3 wks | | | | | | | |
| 25 | | Award | 0 days | Wed 10/7/20 | Wed 10/7/20 | 24FS+3 wks | | | | | | | |
| 26 | | Begin Construction | 0 days | Wed 10/28/20 | Wed 10/28/20 | 25FS+3 wks | | | | | | | |
| 27 | | Construction | 159 wks | Wed 10/28/20 | Wed 11/15/23 | 26 | | | | | | | |
| 28 | | End Construction | 0 days | Wed 11/15/23 | Wed 11/15/23 | 27 | | | | | | | |


Project: Tiger Project Schedule
Date: Fri 10/13/17

| | | | | | |
|--------------------|--|-----------------------|--|--------------------|--|
| Task | | Inactive Summary | | External Tasks | |
| Split | | Manual Task | | External Milestone | |
| Milestone | | Duration-only | | Deadline | |
| Summary | | Manual Summary Rollup | | Progress | |
| Project Summary | | Manual Summary | | Manual Progress | |
| Inactive Task | | Start-only | | | |
| Inactive Milestone | | Finish-only | | | |

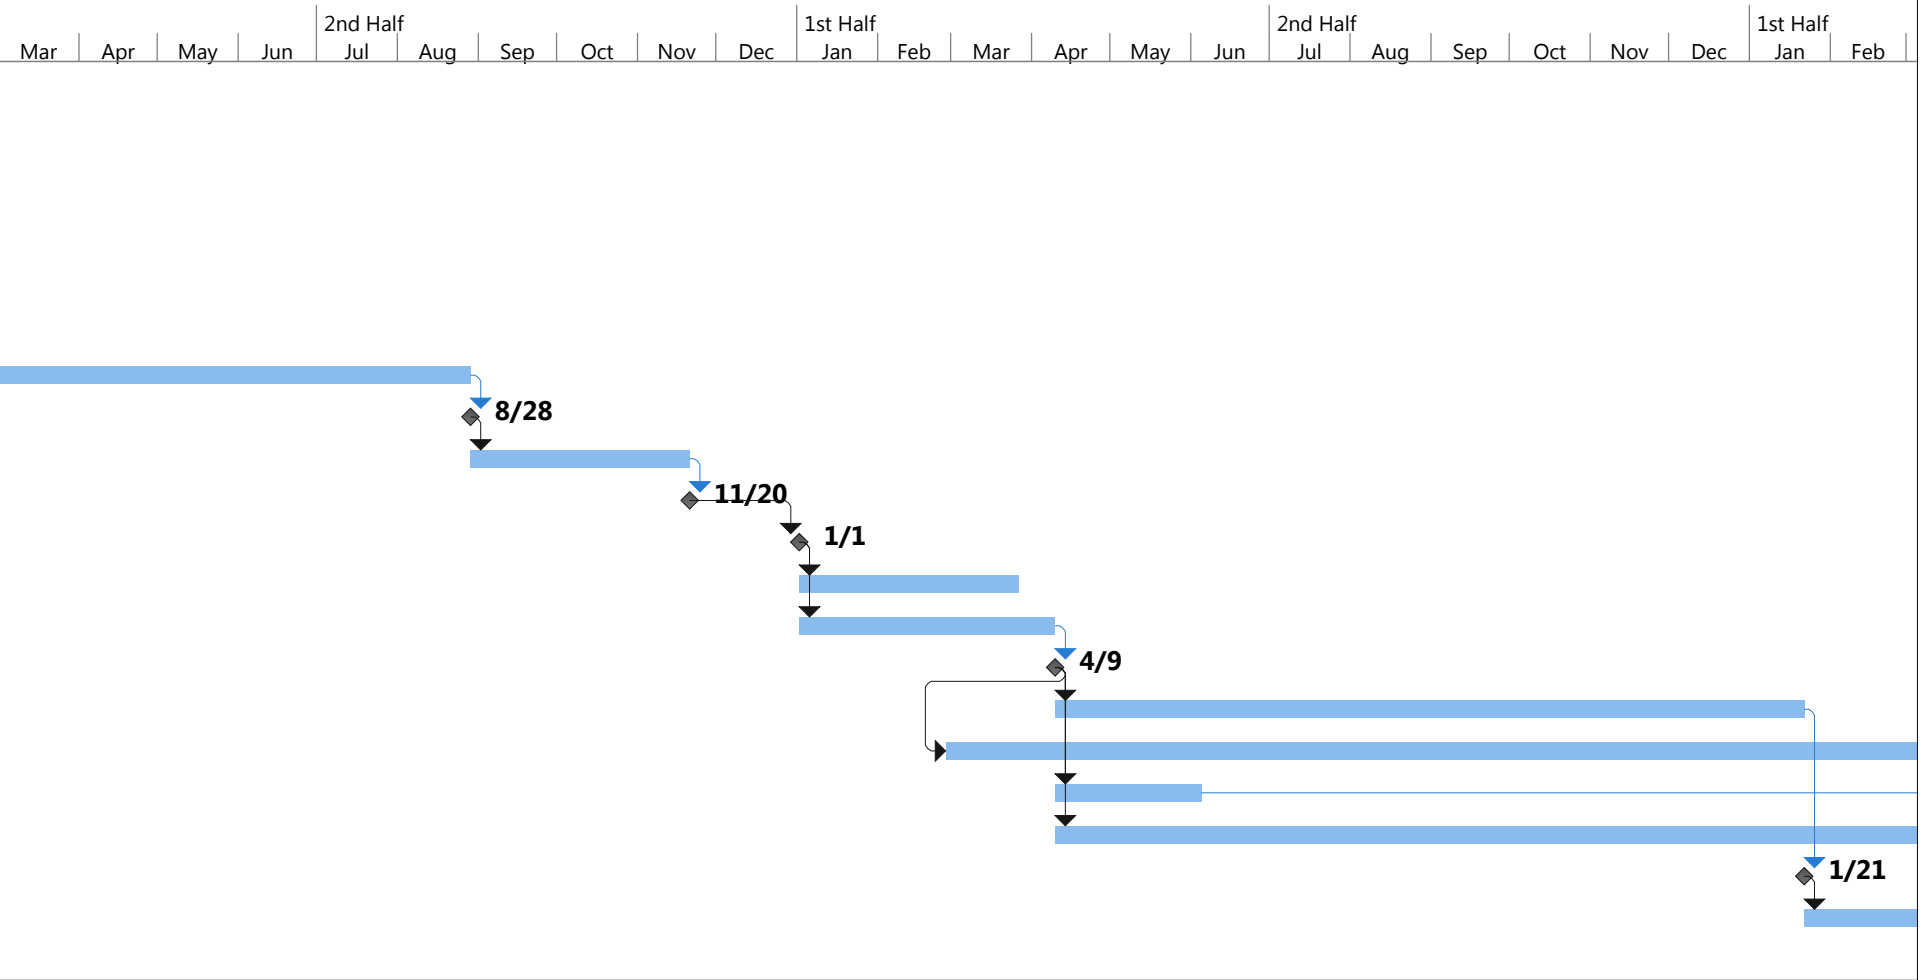





















| | | | | | | |
|---|--------------------|--|-----------------------|--|--------------------|--|
| Project: Tiger Project Schedule Date: Fri 10/13/17 | Task | | Inactive Summary | | External Tasks | |
| | Split | | Manual Task | | External Milestone | |
| | Milestone | | Duration-only | | Deadline | |
| | Summary | | Manual Summary Rollup | | Progress | |
| | Project Summary | | Manual Summary | | Manual Progress | |
| | Inactive Task | | Start-only | | | |
| | Inactive Milestone | | Finish-only | | | |

Mar | Apr | May | Jun | 2nd Half | Jul | Aug | Sep | Oct | Nov | Dec | 1st Half | Jan | Feb | Mar | Apr | May | Jun | 2nd Half | Jul | Aug | Sep | Oct | Nov | Dec | 1st Half | Jan | Feb |




Project: Tiger Project Schedule
Date: Fri 10/13/17


| | | | | | |
|--------------------|---|-----------------------|---|--------------------|---|
| Task |  | Inactive Summary |  | External Tasks |  |
| Split |  | Manual Task |  | External Milestone |  |
| Milestone |  | Duration-only |  | Deadline |  |
| Summary |  | Manual Summary Rollup |  | Progress |  |
| Project Summary |   | Manual Summary |  | Manual Progress |  |
| Inactive Task | | Start-only |  | | |
| Inactive Milestone |  | Finish-only |  | | |

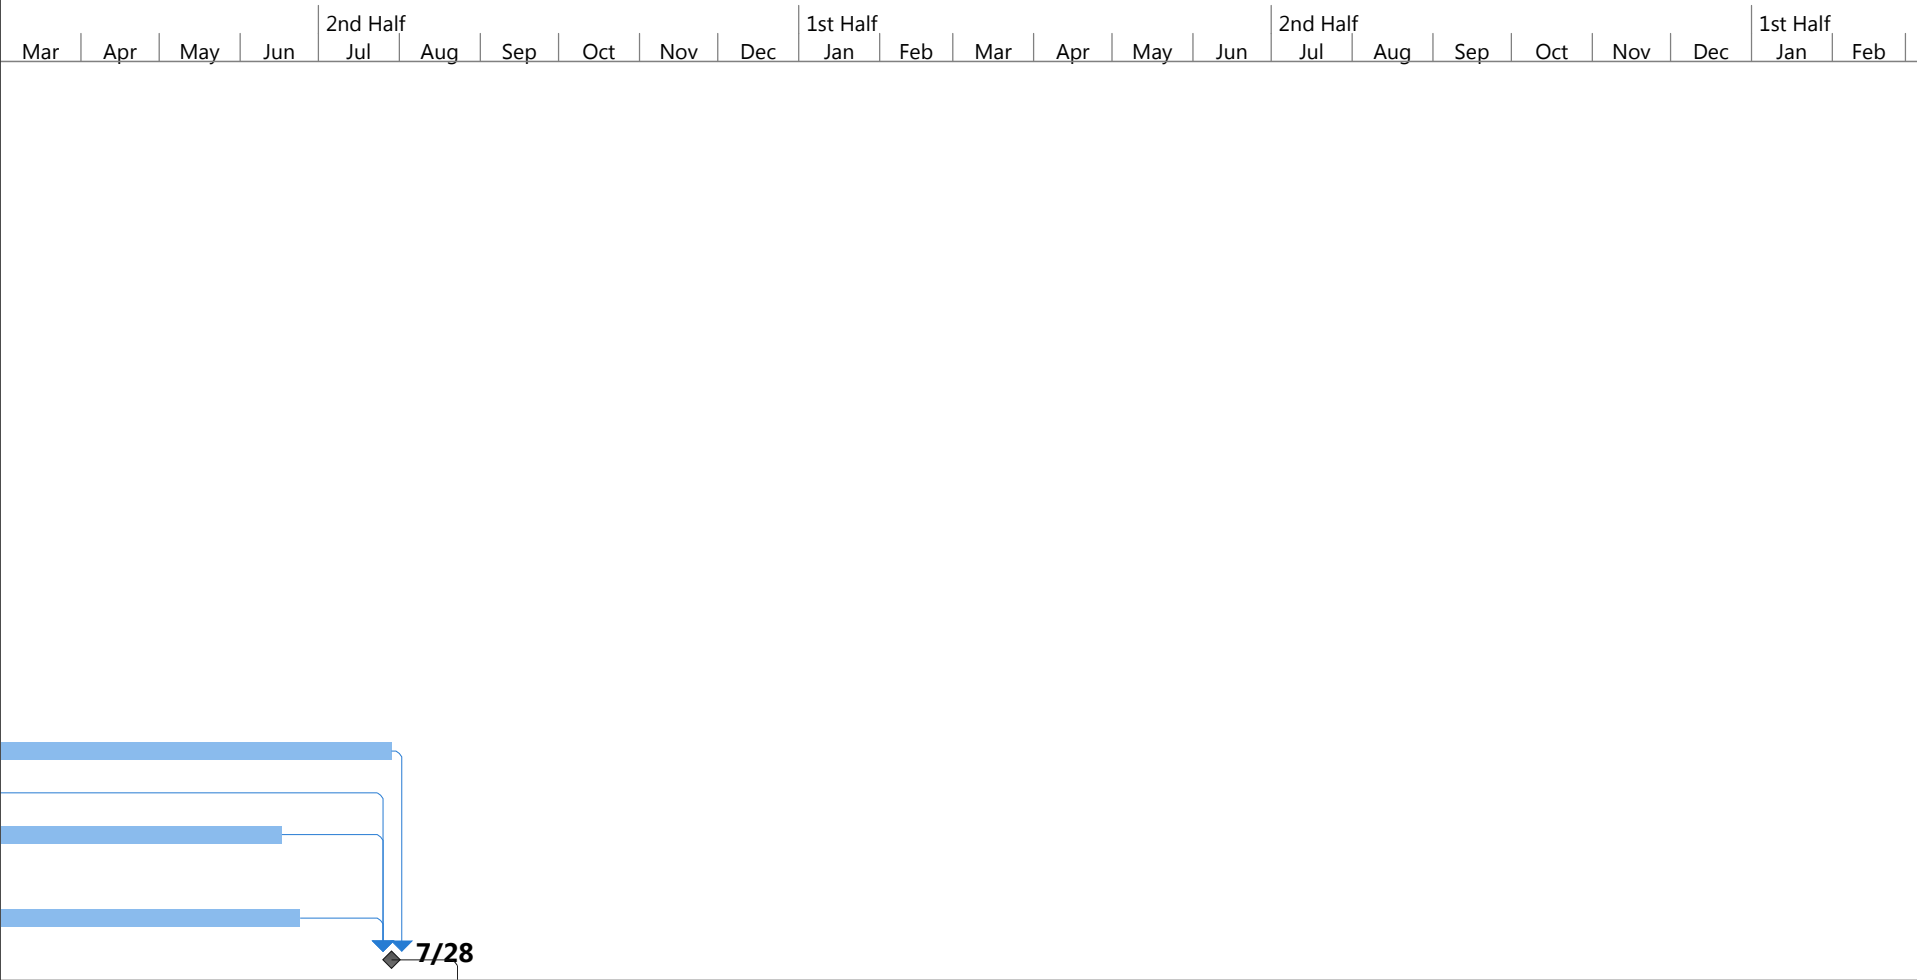

| | | | | | | |
|---|--------------------|--|-----------------------|--|--------------------|--|
| Project: Tiger Project Schedule Date: Fri 10/13/17 | Task | | Inactive Summary | | External Tasks | |
| | Split | | Manual Task | | External Milestone | |
| | Milestone | | Duration-only | | Deadline | |
| | Summary | | Manual Summary Rollup | | Progress | |
| | Project Summary | | Manual Summary | | Manual Progress | |
| | Inactive Task | | Start-only | | | |
| | Inactive Milestone | | Finish-only | | | |

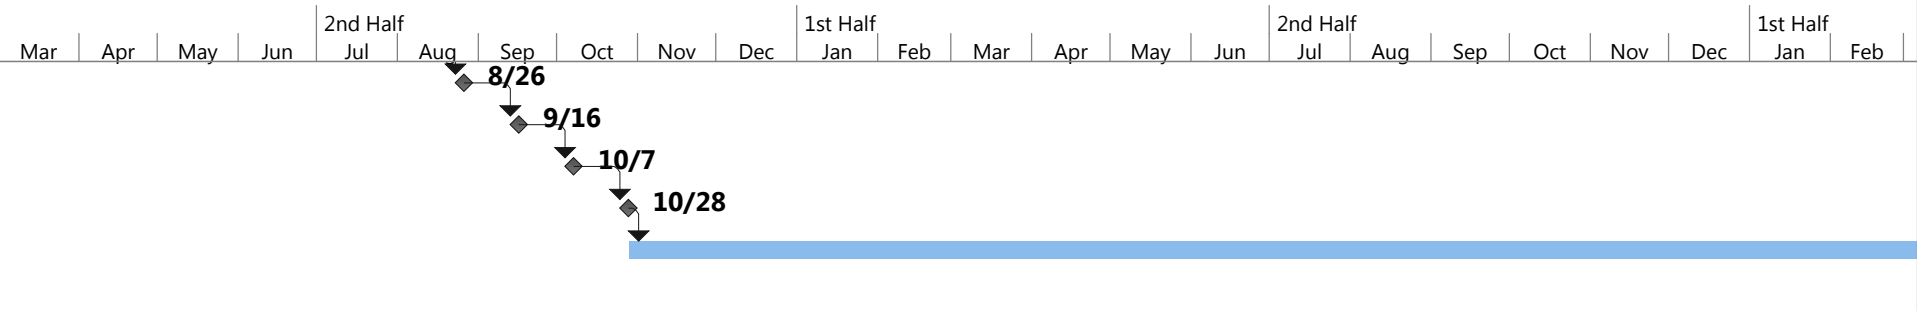


| | | | | | | |
|---|--------------------|--|-----------------------|--|--------------------|--|
| Project: Tiger Project Schedule Date: Fri 10/13/17 | Task | | Inactive Summary | | External Tasks | |
| | Split | | Manual Task | | External Milestone | |
| | Milestone | | Duration-only | | Deadline | |
| | Summary | | Manual Summary Rollup | | Progress | |
| | Project Summary | | Manual Summary | | Manual Progress | |
| | Inactive Task | | Start-only | | | |
| | Inactive Milestone | | Finish-only | | | |



| | | | | | | |
|---|--------------------|--|-----------------------|--|--------------------|--|
| Project: Tiger Project Schedule Date: Fri 10/13/17 | Task | | Inactive Summary | | External Tasks | |
| | Split | | Manual Task | | External Milestone | |
| | Milestone | | Duration-only | | Deadline | |
| | Summary | | Manual Summary Rollup | | Progress | |
| | Project Summary | | Manual Summary | | Manual Progress | |
| | Inactive Task | | Start-only | | | |
| | Inactive Milestone | | Finish-only | | | |

Mar | Apr | May | Jun | 2nd Half | Jul | Aug | Sep | Oct | Nov | Dec | 1st Half | Jan | Feb | Mar | Apr | May | Jun | 2nd Half | Jul | Aug | Sep | Oct | Nov | Dec | 1st Half | Jan | Feb



Project: Tiger Project Schedule
Date: Fri 10/13/17

| | | | | | |
|--------------------|--|-----------------------|--|--------------------|--|
| Task | | Inactive Summary | | External Tasks | |
| Split | | Manual Task | | External Milestone | |
| Milestone | | Duration-only | | Deadline | |
| Summary | | Manual Summary Rollup | | Progress | |
| Project Summary | | Manual Summary | | Manual Progress | |
| Inactive Task | | Start-only | | | |
| Inactive Milestone | | Finish-only | | | |
